

## **PROGRESS BHUBANESWAR AS ON 20 AUG 18**

1. Dismantling and removing of Batching plant 100% completed,
2. **External Development Work**
  - (a) Roads works completed
  - (b) Drains work completed.
  - (c) Cable laying completed.
  - (d) Fixing of street lights except 2 nos completed these 2 nos poles are to be installed at temporary substation of M/s OICL. The same shall be completed after removal of temporary substation.
3. **Lift Work**: Commissioning of Lifts, all 07 blocks completed.
4. **Swimming Pool**: Civil work completed, Tile work is in progress EDC 30 Aug 18.
5. **STP**: Civil work and mechanical installation completed. Testing completed.
6. **Towers**: Balance works of firefighting, paintings in few flats are in progress. No major work pending. Testing and commissioning of all services is in progress.
7. **Energization of Sub Station**: Medium Voltage (MV) Inspection by CESU authority undertaken on 19 May 18 for substations and other electro mechanical items. Energization of substation is completed.
8. **Status of Completion/Occupancy Certificate**: NOCs from CESU, BMC obtained, inspection by PH & MOEF completed, compliance report obtained, initial inspection by fire Dept also completed. EDC 30 Aug 18. On receipt of all NOCs, application for OC will be made to BDA.
9. **Possession**: Handing over of DUs commenced from 18 May 18. 33 Nos Dus have been handing over.(30-Officer Block, 3-Sailor Block)
10. Handing over of Block F and C DU commenced w.e.f. 30 Jul 18.
11. Average daily labour strength at site during July 18 – August 18 is 130.

## **PROGRESS BHUBANESWAR AS ON 20 AUG 18**



### **TOWER NO: A OFFICERS (Overall completion-99.65%)**

Total floors: S1+S2+8

Total Flats: 32

### **PROGRESS:**

<b>CHINA WARE FITTING</b>	- 100% completed
<b>PAINTING (INTERNAL)</b>	- 100% (Final paint completed)
<b>EXTERNAL PAINT</b>	- 100% completed
<b>ELECTRICAL WORK</b>	- 100% completed
<b>DOOR &amp; WINDOW FIXING</b>	- 100% completed
<b>FIRE FIGHTING WORK</b>	- 98% completed
<b>CP FITTING</b>	- 100% completed

## **PROGRESS BHUBANESWAR AS ON 20 AUG 18**



### **TOWER NO: B OFFICERS (Overall completion-99.00%)**

Total floors: S1+S2+8

Total Flats: 32

### **PROGRESS:**

<b>PLUMBING</b>	- 100% completed
<b>EXTERNAL PAINT</b>	-100% completed
<b>ELECTRICAL WORK</b>	- 100% completed
<b>FIRE FIGHTING WORK</b>	- 97% completed
<b>DOOR &amp; WINDOW FIXING</b>	- 100% completed
<b>CHINA WARE FITTING</b>	- 100% completed

## **PROGRESS BHUBANESWAR AS ON 20 AUG 18**



**TOWER NO: C OFFICERS (Overall completion-98.50%)**

Total floors: S1+S2+8

Total Flats: 32

**PROGRESS:**

<b>PLUMBING</b>	- 100% completed
<b>CHINA WARE FITTING</b>	- 100% completed
<b>EXTERNAL PAINT</b>	-100% completed
<b>ELECTRICAL WORK</b>	- 100% completed
<b>DOOR &amp; WINDOW FIXING-</b>	100% completed
<b>FIRE FIGHTING WORK</b>	- 97% completed

## PROGRESS BHUBANESWAR AS ON 20 AUG 18



### **TOWER NO: D OFFICERS (Overall completion-99%)**

Total floors: S1+S2+8

Total Flats: 32

### **PROGRESS:**

<b>CHINA WARE FITTING</b>	- 100% completed
<b>EXTERNAL PAINT</b>	-100% completed
<b>ELECTRICAL WORK</b>	- 100% completed
<b>DOOR &amp; WINDOW FIXING</b>	- 100% completed
<b>FIRE FIGHTING WORK</b>	- 97% completed
<b>CP FITTING</b>	-100% completed

## PROGRESS BHUBANESWAR AS ON 20 AUG 18



**TOWER NO: E SAILOR (Overall completion-98.50%)**

Total floors: S1+S2+11

Total Flats: 43

**PROGRESS:**

<b>EXTERNAL PAINT</b>	- 100% completed
<b>PLUMBING</b>	- 100% completed
<b>ELECTRICAL WORK</b>	- 100% completed
<b>FIRE FIGHTING WORK</b>	- 97% completed
<b>DOOR &amp; WINDOW FIXING</b>	- 100% completed
<b>CHINA WARE FITTING</b>	- 100% completed

## PROGRESS BHUBANESWAR AS ON 20 AUG 18



### **TOWER NO: F SAILOR (Overall completion-96.00%)**

Total floors: S1+S2+11

Total Flats: 43

### **PROGRESS:**

<b>TILING</b>	- 100% completed
<b>PLUMBING</b>	- 85% completed
<b>EXTERNAL PAINT</b>	-100% completed
<b>ELECTRICAL WORK</b>	- 100% completed
<b>FIRE FIGHTING WORK</b>	-97% completed
<b>DOOR &amp; WINDOW FIXING</b>	- 100% completed
<b>STAIRCASE RAILING</b>	-100% completed
<b>FALSE CEILING</b>	-100% Completed

## PROGRESS BHUBANESWAR AS ON 20 AUG 18



**TOWER NO: G SAILOR (Overall completion-99.7%)**

Total floors: S1+S2+11

Total Flats: 42

**PROGRESS:**

<b>EXTERNAL PAINT</b>	- 100% completed
<b>CHINA WIRE FITTING</b>	- 100% completed
<b>ELECTRICAL WORK</b>	- 100% completed
<b>FIRE FIGHTING WORK</b>	- 97% completed
<b>CP FITTING</b>	- 100% completed

## **PROGRESS BHUBANESWAR AS ON 20 AUG 18**



### **TOWER NO: COMMUNITY CENTER (Overall completion-96.80%)**

Total floors: G+1

### **PROGRESS:**

<b>BRICK WORK</b>	- 100% completed
<b>PAINTING</b>	- 100% (1 <sup>st</sup> coat paint completed)
<b>ELECTRICAL WORK</b>	- 95% completed
<b>FIRE FIGHTING WORK</b>	- 90% completed
<b>DOOR &amp; WINDOW FIXING</b>	- 60% completed
<b>EXTERNAL PAINT</b>	- 75% completed
<b>TILING</b>	- 80% completed

## PROGRESS BHUBANESWAR AS ON 20 AUG 18

### SWIMMING POOL



**SWIMMING POOL-** (Overall completion- 95%)

**PROGRESS:** - Mosaic Tile Work completed.

- Deck area tile work.

## **PROGRESS BHUBANESWAR AS ON 20 AUG 18**

### **ELECTRICAL WORK AT SITE**



**PROGRESS:** - Focus lamp fixing at terrace area

## **PROGRESS BHUBANESWAR AS ON 20 AUG 18**

### **EXTERNAL ELECTRICAL WORK AT CESU PREMISES (A)**



**CABLE TRENCH COVERING IN SIDE AFNHB**



**CABLE END TERMINATION IN SIDE AFNHB**




**EXTERNAL ELECTRICAL (PART-A) - (Overall completion- 97%)**

**PROGRESS:** All works completed. Common load charging completed.

**PROGRESS BHUBANESWAR AS ON 20 AUG 18**

**EXTERNAL ELECTRICAL WORK AT AFNHB SITE PREMISES (B)**

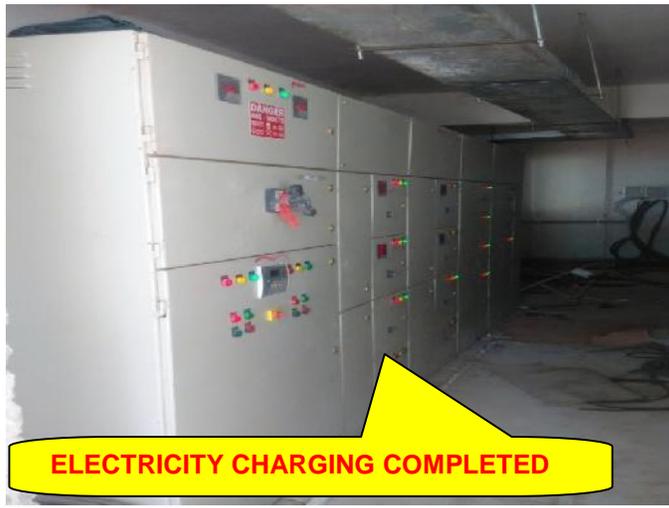

**EXTERNAL ELECTRICAL (PART-B) - (Overall completion- 98%)**

**PROGRESS:**

- |                              |                                      |
|------------------------------|--------------------------------------|
| <b>CIVIL FOUNDATIONS</b>     | - 98% completed                      |
| <b>EQUIPMENT ERECTION</b>    | - 100% completed                     |
| <b>STRUCTURE ERECTION</b>    | - FP & TP erected                    |
| <b>CABLE LAYING</b>          | - 100% completed                     |
| <b>CABLE END TERMINATION</b> | - 99% completed                      |
| <b>LT PANEL</b>              | - 100% Completed                     |
| <b>LIGHTNING ARRESTOR</b>    | - 100% Completed)                    |
| <b>STREET LIGHT</b>          | - 85% Completed                      |
| <b>TELEPHONE SYSTEM</b>      | - Telephone cabling work in progress |
| <b>TESTING</b>               | -IR TEST completed                   |
