

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017

AVERAGE DAILY LABOUR FEB 2017: 320



TOWER-1 (TYPE A-1) (Overall completion 91.30 %)

Total Floor – Stilt + 10

Total flat = 60

Progress – Anti termite & PCC at stilt floor and Glass fixing in Aluminum windows.

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017



TILE FLOORING

TOWER 2 (TYPE A-1) (Overall completion 75.10 %)

Total Floor – Stilt + 10

Total flat = 60

Progress – Casting of top slab of OH water tank, Vitrified tiles fixing in bed rooms, water proofing of toilets, kitchens, balconies & lift pit, plumbing work in shafts & toilets.

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017



EXTERNAL PLASTER

INTERNAL PLASTER

TOWER-3 (TYPE A-1) (Overall completion 63.30 %)

Total Floor – Stilt + 10

Total flat = 60

Progress – External & Internal plaster, door frame fixing, brick work of parapet wall & plumbing shaft.

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017



BRICK WORK IN TERRACE

TOWER-4 (TYPE A-1) (Overall completion 62.82 %)

Total Floor – Stilt + 10

Total flat = 60

Progress – Fixing of railing in balconies & brick work in front elevation and parapet.

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017



EXTERNAL PLASTERING

TOWER-5 (TYPE A-2) (Overall completion 67.39 %)

Total Floor – Stilt + 10

Total flat = 60

Progress – External plaster of flat 3, internal plaster at 10th floor, Casting of terrace floor column, shuttering of bottom slab of machine room & OH Water tank.

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017



TILE FIXING INSIDE OH TANK



KOBA WORK IN TERRACE

TOWER-6 (TYPE A-2) (Overall completion 84.61 %)

Total Floor – Stilt + 10

Total flat = 60

Progress –Fixing of Ceramic tiles in OH water tank, Terrace Koba & plaster repairing work.

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017



CORRIDOR & STAIR CASE GREEN MARBLE FIXING

TOWER-7 (TYPE B-1) (Overall completion 84.61 %)

Total Floor – Stilt + 11

Total flat = 119

Progress – External plaster in part-I, wall tiles fixing in toilets, Granite fixing on wash basin counters, Green marble fixing in staircase, Aluminum frame fixing in windows.

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017



**BRICK WORK STILT FLOOR
PENDING WORKS**

TOWER- 8 (TYPE B-1 & TYPE B2) (Overall completion 86.60 %)

Total Floor – Stilt + 11

Total flat = 33

Progress – Brick work repairing at stilt floor, Glass fixing in Aluminium windows.

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017



EXTERNAL PAINTING IN PROGRESS

COMMUNITY CENTRE - (Overall completion 90.00 %)

Total floor – Basement +03

Progress – External primer in progress.

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017



FACILITY BLOCK - (Overall completion 95.15 %)
Total floor - Ground +01
Progress - No progress.

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017




**Gate No. 1 – (Overall Completion 90.00 %)
Progress- Road Work in Progress**

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017



**STP - (Overall Completion 37.26 %)
Progress- No Progress**

PROGRESS MEERUT PROJECT AS ON 23 FEB 2017

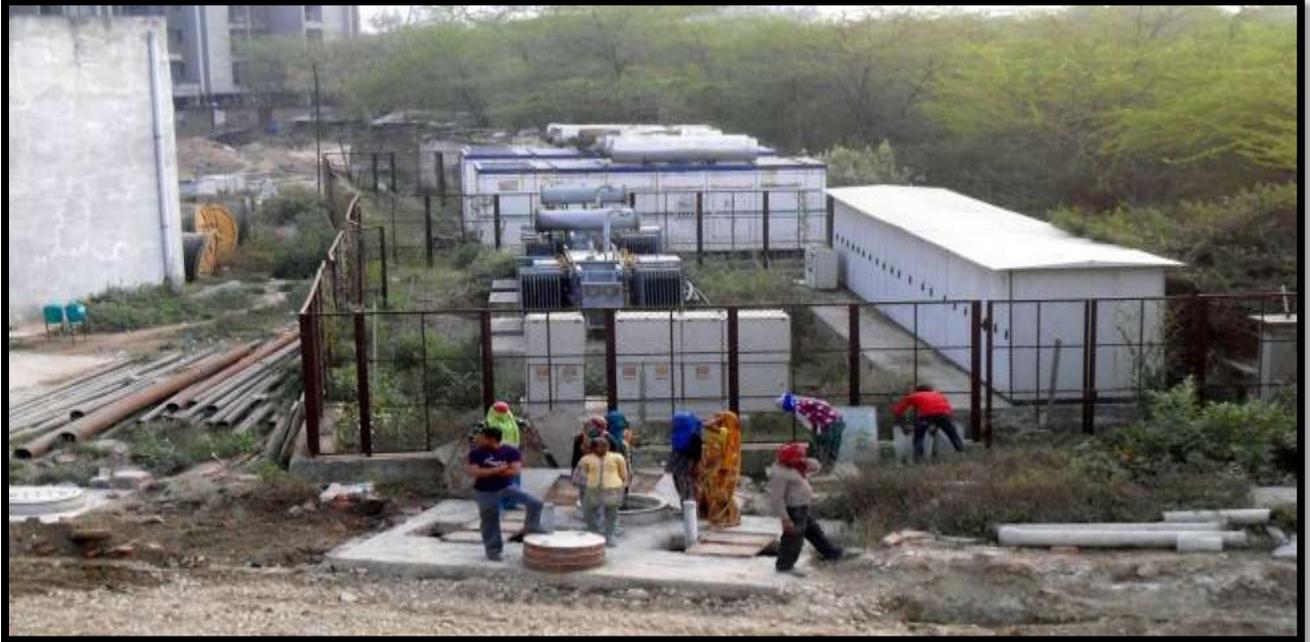

Power House - (Overall Completion 96.00 %)
Progress - Generators, Transformers, HT/LT cables and control Panels Procured, Awaiting Energizing, Laying of cables in progress.
