

**AFNHB JAIPUR PH-II PROJECT**  
**WKS/001/24 DATED 30 AUG 24**  
**WORK PROGRESS UPTO AUG 24 TOWER - B**



**INTERNAL FINISHING IN PROGRESS**




1. MACHINE ROOM RCC SLAB, MUMTY, PERGOLA COMPLETE AND OVER HEAD WATER TANK WORK IN PROGRESS.
2. MACHINE ROOM BRICK WORK IN PROGRESS.
3. BRICK WORK UP TO 8<sup>TH</sup> FLOOR COMPLETED, 9<sup>TH</sup> FLOOR IN PROGRESS.
4. ELECTRICAL WORK 8<sup>TH</sup> FLOOR IN PROGRESS.
5. DOOR FRAME UP TO 8<sup>RD</sup> FLOOR COMPLETED.
6. PLUMBING WORK IN 8<sup>TH</sup> FLOOR COMPLETED AND 9<sup>TH</sup> FLOOR IN PROGRESS.
7. INTERNAL PLASTER UP TO 6<sup>TH</sup> FLOOR COMPLETED AND 7<sup>ND</sup> FLOOR UNDER PROGRESS.
8. WATER PROOFING IN 7<sup>TH</sup> FLOOR UNDER PROGRESS.
9. TILE WORK 6<sup>TH</sup> FLOOR IN PROGRESS.
10. INTERNAL PAINTING 6<sup>TH</sup> FLOOR IN PROGRESS.
11. EXTERNAL PLASTER IN PROGRESS.
12. LIFT MATERIAL ARRIVED AT SITE.
13. FIRE FIGHTING WORK IN PROGRESS
14. EDC END DEC24 FOR COMMENCEMENT OF H/O OF DUs.

**AFNHB JAIPUR PH-II PROJECT**  
**WORK PROGRESS UPDATE UP TO AUG 24 TOWER - G**



**INTERNALFINISHING IN PROGRESS**

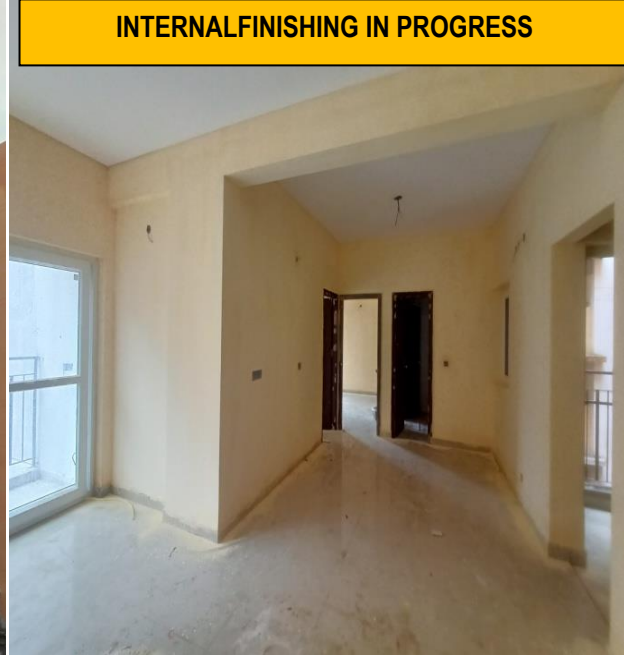

1. **INTERNAL PAINT 1ST COAT 36 FLAT COMPLETED.**
2. **ALL TILE FLOORING AND KITCHEN COUNTER TOP GRANITE COMPLETED.**
3. **ELECTRICAL WIRING IN 34 FLAT COMPLETED, REMAINING WORK IN PROGRESS.**
4. **SUB-MAIN WIRING & FLATS SWITCH SOCKET FIXING WORK IN PROGRESS.**
5. **PLUMBING WORK COMPLETED.**
6. **FITMENT OF MS GRILLS AND RAILING IN BALCONY WORK COMPLETED.**
7. **DOOR SHUTTER FIXING COMPLETED.**
8. **UPVC DOORS & WINDOWS HARDWARE FIXING IN PROGRESS.**
9. **SANITARY WARE FIXING IN PROGRESS**
10. **FALSE CEILING WORKS IN PROGRESS IN TOILETS.**
11. **TERRACE WATER PROOFING COBA FINISHING WING NO. 01, 02 & 04 COMPLETED AND WING NO 03 IN PROGRESS.**
12. **EXTERNAL PAINT 75 % COMPLETED AND TEXTURE PAINT IN PROGRESS.**
13. **LIFT MECHANICAL WORK COMPLETED & CLADDING WORK IN PROGRESS.**
14. **WHITE WASH IN PROGRESS IN STILT AREA.**
15. **FIRE FIGHTING WORK IN PROGRESS**
16. **EDC END OCT 24 FOR COMMENCEMENT OF H/O IN NOV 24.**

**AFNHB JAIPUR PH-II PROJECT**  
**WORK PROGRESS UP TO AUG 24 TOWER - K**



**FLAT INSIDE WORK IN PROGRESS**

- 1. RCC SLAB IN 7TH FLOOR ROOF 3 FLAT COMPLETED & BALANCE 3 FLATS SHUTTERING WORK IN PROGRESS.**
- 2. BRICK WORK 1ST, 2ND & 3 RD FLOOR 90 % COMPLETED AND 5TH FLOOR 2 FLATS IN PROGRESS.**
- 3. ELECTRICAL WALL CONDUIT WORK IN PROGRESS.**
- 4. FITMENT OF DOOR FRAME HAS COMMENCED**
- 5. INTERNAL PLUMBING WORK IN 1ST TO 3RD FLOOR COMPLETED**
- 6. EDC MAR 2025**

## **STATUS OF NOC'S AND OTHER CLEARANCES.**

### **TOWER- A**

- 1. FLATS HANDED OVER - 33/36**
- 2. EXTERNAL SERVICES COMPLETED**
- 3. FIRE NOC OBTAINED FOR TOWER-A**
- 4. ENVIORNMENT CLEARANCE OF ENTIRE PROJECT HAS OBTAINED**
- 5. CTO FROM POLLUTION CONTROL BOARD REPORT PREPARED BY CONSULTANT IS READY FOR SUBMISSION**
- 6. COMPLETION CERTIFICATE FOR TOWER A- CC & OC OBTAINED**
- 7. ELECTRICITY - JVVNL CONNECTED**
- 8. DRAINAGE & SEWER WORK COMPLETED AND CONNECTED TO STP**
- 9. LIFTS- TOWER A READY, RWA HAS REQUESTED TO TAKE OVER**
